



# AACE-PSP<sup>Q&As</sup>

Planning & Scheduling Professional (PSP)

## Pass AACE International AACE-PSP Exam with 100% Guarantee

Free Download Real Questions & Answers **PDF** and **VCE** file from:

<https://www.pass4itsure.com/aace-psp.html>

100% Passing Guarantee  
100% Money Back Assurance

Following Questions and Answers are all new published by AACE International Official Exam Center

- ⚙️ **Instant Download** After Purchase
- ⚙️ **100% Money Back** Guarantee
- ⚙️ **365 Days** Free Update
- ⚙️ **800,000+** Satisfied Customers





### QUESTION 1

Based on the stated costs, what percentage of the total cost comes from the 2000 series of activities?

- A. 3.9% (1 : 25.708)
- B. 2.3% (1 : 43.501).
- C. 9.1% (1 : 11.000).
- D. 8.6% (1 : 11.591)

Correct Answer: B

---


### QUESTION 2

The activity with the most total float is:



Refer to the following table and diagram to answer the following questions. Consider this to be the entire network. The diagram is incomplete. This table represents activities, predecessors and durations for a hazardous waste incineration facility:

Activity	Description	Predecessors	Duration (months)
A	Develop information for public hearings		3
B	Hold public hearings	A	3
C	Develop draft plans and specifications	A	5
D	Contact stakeholders and others	A	7
E	Obtain permits	B, C	3
F	Order equipment for facility	B	4
G	Procure and prepare land.	B	6
H	Construct facility	D, E, F & G	8
I	Approval of operating procedures	D	6
J	Install equipment, staff, faculty	F	9

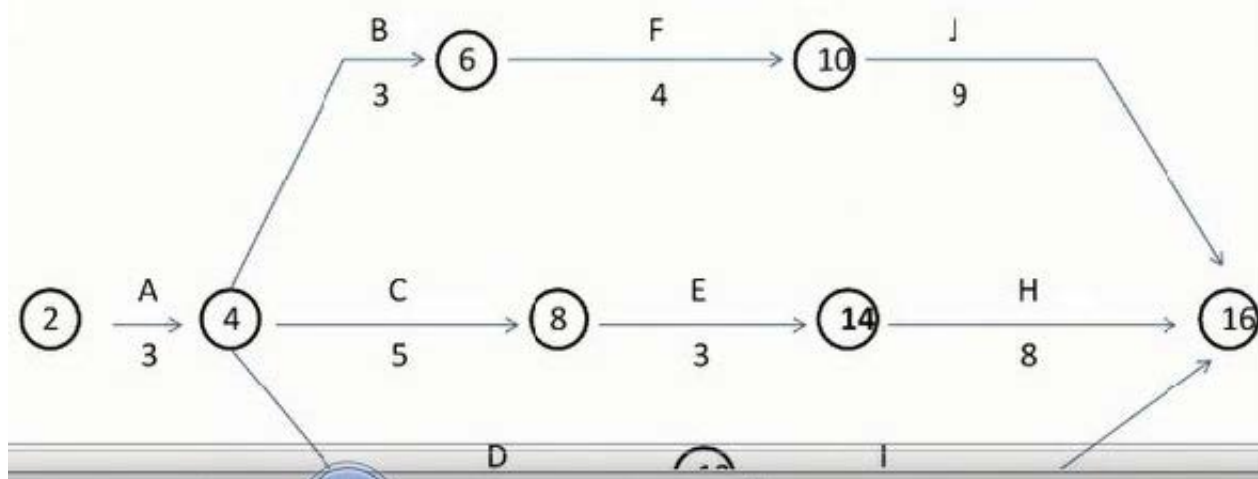

A. Activity I.

B. Activity C.

C. Activity F.

D. Activity D.

Correct Answer: A

### QUESTION 3

At the end of month one, did the delay to the parking structure foundation delay the project?

A. NO.



- B. Yes, by 4 calendar days.
- C. Yes, by 14 calendar days.
- D. Yes, by 9 calendar days.

Correct Answer: B

---

#### QUESTION 4

The linear scheduling velocity diagram has the following two-axis:

- A. Location and crew size
- B. Time and location
- C. Time and rate of progress
- D. Time and crew size

Correct Answer: C

---

#### QUESTION 5

What owner action could have mitigated the late completion of the project?

- A. Hire a more senior project manager.
- B. Self-perform more of the work.
- C. Use a procurement agent to monitor and expedite equipment deliveries.
- D. Prepare better structural steel drawings.

Correct Answer: C

[AACE-PSP VCE Dumps](#)

[AACE-PSP Study Guide](#)

[AACE-PSP Braindumps](#)
