



PRINCE2-PRACTITIONER^{Q&As}

PRINCE2 Practitioner

**Pass PRINCE2 PRINCE2-PRACTITIONER Exam with
100% Guarantee**

Free Download Real Questions & Answers **PDF** and **VCE** file from:

<https://www.pass4itsure.com/prince2-practitioner-1.html>

100% Passing Guarantee
100% Money Back Assurance

Following Questions and Answers are all new published by PRINCE2
Official Exam Center

-  **Instant Download** After Purchase
-  **100% Money Back** Guarantee
-  **365 Days** Free Update
-  **800,000+** Satisfied Customers





QUESTION 1

DRAG DROP

RISK

The following risk has been identified during a risk identification workshop:

"Because the project is reliant on the government agency accrediting the classroom-based training materials before work can continue on the project, there is a risk that the accreditation will either be withheld or delayed, leading to a delay in

the overall project with associated cost implications."

Here are three items of information that will be included in the risk register about this risk.

Under which heading (A-F) should they be recorded?

Choose only ONE heading for each item of information. Each heading can be used once, more than once, or not at all.

Select and Place:


Risk status	Probability, impact and expected value
Risk owner	Proximity
Risk actionee	Risk response

The accrediting agency will be involved throughout stage 2 by having ongoing discussions and releasing of early drafts to ensure a smooth accreditation

The Business Development Director will be responsible for monitoring and reporting on the progress of accreditation and the impact this might have on costs

This risk could occur in the last few weeks of stage 3

Correct Answer:

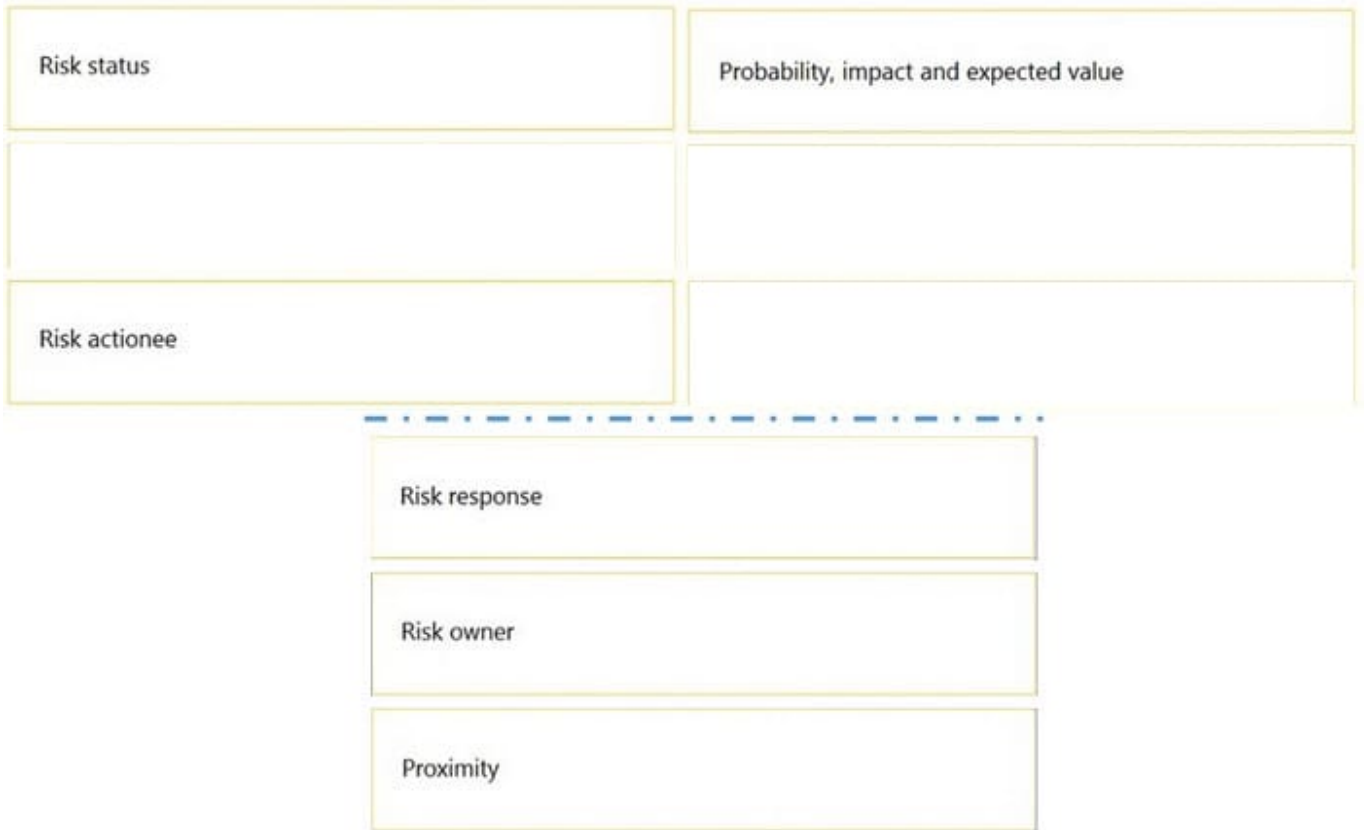

QUESTION 2

Which of the following activities is NOT an action of preparing for planned closure?

- A. Update the project plan with actual
- B. Update the Project Management Team
- C. Request a product status account
- D. Confirm project has delivered what is defined in Project Product Description

Correct Answer: B

QUESTION 3

MANAGING A STAGE BOUNDARY

The project is approaching the end of stage 3 and the pilot courses have been planned. The project manager is now undertaking the 'managing a stage boundary' process. Which action should the project manager undertake as part of the 'update the business case' activity?

- A. Identify the dependencies between the activities required to run the 'delivered pilot courses' during stage 4.
- B. Revise the overall plan and resources to complete the project, based on actuals from the stage 3 plan.



C. Review the performance of the external suppliers who worked on delivery of the 'e-learning course' during stage 3.

D. Re-plan when the number of learners using the pilot course, and their increased knowledge, will be measured during stage 4.

Correct Answer: A

QUESTION 4

DRAG DROP

PLANS

The project manager is preparing the stage 3 plan and has asked the team manager for the 'amended course booking procedures' work package to prepare the team plan at the same time.

Here are three actions that will need to be carried out when preparing these plans.

Which role (A-F) should be responsible for each action?

Choose only ONE role for each action. Each role can be used once, more than once, or not at all.

Select and Place:



Executive

Senior user

Project manager

Team manager

Project assurance

Project support

Provide assistance with using the planning software package when the plan for the 'amended course booking procedures' is being prepared

Provide an expert from the Sales Team to identify the impact that the 'amended course booking procedures' will have on sales staff

Timetable the tasks to deliver the 'amended course booking procedures' and allocate them to specific individuals

Correct Answer:



Executive

Senior user

Project assurance

Team manager

Project manager

Project support

QUESTION 5



Which of the following is NOT an objective of Initiating a Project?

- A. Understanding the scope of what is to be done and the products to be delivered
- B. Understanding the roles and responsibilities of the Project Management Team
- C. Understand how quality required will be achieved
- D. Understand how progress will be monitored and controlled

Correct Answer: B

[Latest PRINCE2-PRACTITIONER Dumps](#)

[PRINCE2-PRACTITIONER VCE Dumps](#)

[PRINCE2-PRACTITIONER Study Guide](#)
